


File Edit View Insert Format Tools Project Report Collaborate Window Help

Type a question for help

No Group Arial 10 B I U

ID	Task Name	Duration	Start	Finish	Predecessors	Resou
0	PracticeEx Claire Couillard	110 days	Thu 3/18/10	Wed 8/18/10		
1	1 Design Phase	25 days	Thu 3/18/10	Wed 4/21/10		
2	1.1 Design Feasibility Study	10 days	Thu 3/18/10	Wed 3/31/10		Design
3	1.2 Design/Analysis	15 days	Thu 4/1/10	Wed 4/21/10	2	Design
4	2 Build Prototype Phase	25 days	Thu 4/1/10	Wed 5/5/10		
5	2.1 1st Generation Build	10 days	Thu 4/1/10	Wed 4/14/10	2	Produ
6	2.2 Competitive Engine Evalu	15 days	Thu 4/15/10	Wed 5/5/10	5	Design
7	2.3 Customer Input	5 days	Thu 4/15/10	Wed 4/21/10	5	Produ
8	3 Test Phase	75 days	Thu 5/6/10	Wed 8/18/10		
9	3.1 1st Life Test	30 days	Thu 5/6/10	Wed 6/16/10	3,6,7	Test T
10	3.2 Final Design and Life Tes	15 days	Thu 6/17/10	Wed 7/7/10	9	Design
11	3.3 Performance Developme	8 days	Thu 7/8/10	Mon 7/19/10	10	Design
12	3.4 Field Testing	30 days	Thu 7/8/10	Wed 8/18/10	10	Test T
13	4 Production Rollout	0 days	Wed 8/18/10	Wed 8/18/10	11,12	

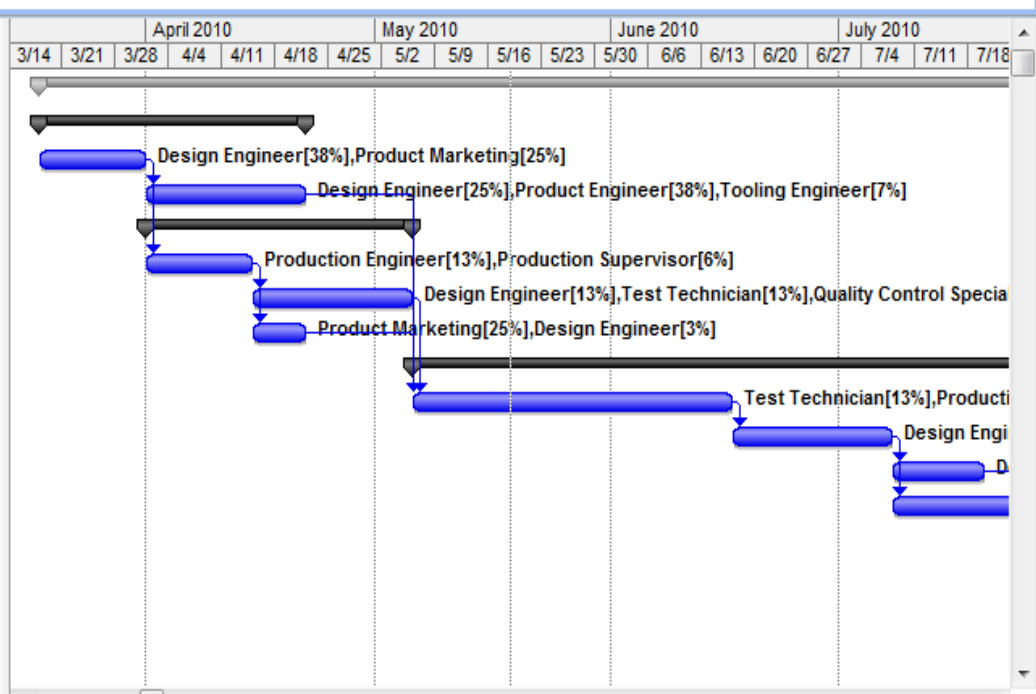

Name: PracticeEx Claire Couillard 10.03.18 Duration: 110d  Effort driven Previous Next

Start: Thu 3/18/10 Finish: Wed 8/18/10 Task type: Fixed Duration % Complete: 0%

ID	Resource Name	Units	Work	ID	Predecessor Name	Type	Lag
