Microsoft Project - Pole Shed Project Claire Couillard 10.03.18

File Edit View Insert Format Tools Project Report Collaborate Window Help

Gantt Chart

	Task Name	Duration	Start	Finish	Predecessors	Resource Names
0	Pole Shed Project Claire Cou	9.5 days	Tue 3/16/10	Mon 5/24/10		
1	1 Preparation Phase	4 days	Tue 3/16/10	Fri 3/19/10		
2	1.1 Survey	1 day	Tue 3/16/10	Tue 3/16/10		Engineer[40%],S
3	1.2 Buy Building Permit	1 day	Wed 3/17/10	Wed 3/17/10	2	Purchasing Ager
4	1.3 Purchase Pole Shed	1 day	Thu 3/18/10	Thu 3/18/10	3	Purchasing Ager
5	1.4 Receive Delivered Pole Shed	1 day	Fri 3/19/10	Fri 3/19/10	4	Purchasing Ager
6	2 Construction Phase	43 days	Mon 3/22/10	Wed 5/19/10		
7	2.1 Dig Foundation	2 days	Mon 3/22/10	Tue 3/23/10	5	Operator,Engine
8	2.2 Pour Cement Slab	1 day	Wed 3/24/10	Wed 3/24/10	7	Operator[50%],C
9	2.3 Construct Pole Shed Frame	5 days	Thu 3/25/10	Wed 3/31/10	8	Construction Cre
10	2.4 Construct Pole Shed Roof	5 days	Thu 4/1/10	Wed 4/7/10	9	Construction Cre
11	2.5 Construct Pole Shed Sides	10 days	Thu 4/8/10	Wed 4/21/10	10	Construction Cre
12	2.6 Install Electricity	10 days	Thu 4/22/10	Wed 5/5/10	11	Electrician
13	2.7 Install Plumbing	10 days	Thu 5/6/10	Wed 5/19/10	12	Plumber
14	3 Inspection Phase	2.5 days	Thu 5/20/10	Mon 5/24/10		
15	3.1 Clean Up Area	2 days	Thu 5/20/10	Fri 5/21/10	13	Cleanup Crew
16	3.2 Inspect Pole Shed	0.5 days	Mon 5/24/10	Mon 5/24/10	15	Inspector,Engine
17	4 Pole Shed Ready for Use	0 days	Mon 5/24/10	Mon 5/24/10	16	

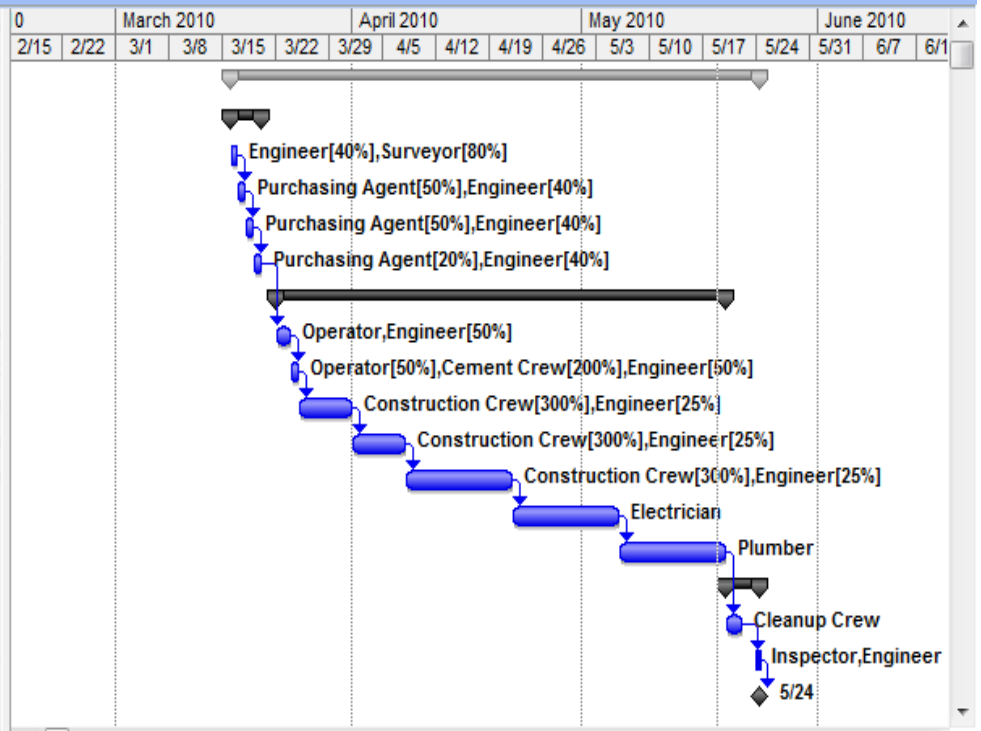

Task Form

Name: Pole Shed Project Claire Couillard 10.03 Duration: 49.5d Effort driven Previous Next

Start: Tue 3/16/10 Finish: Mon 5/24/10 Task type: Fixed Duration % Complete: 0%

ID	Resource Name	Units	Work

ID	Predecessor Name	Type	Lag

Ready

Adobe Dreamweave... Claire Couillard's Po... Document1 - Micro... INMGT 565 Microsoft Project - ... 3:52 PM
